



ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Sep 22, '24												
								W	T	F	S	S	M	T	W	T	F			
1																				
2		Interior Work	64 days	Mon 2/3/25	Thu 5/1/25															
3		Sitework	5 days	Thu 4/3/25	Wed 4/9/25															
4		Micropiles/Concrete	30 days	Wed 4/9/25	Tue 5/20/25	3														
5		Exterior Ductwork	15 days	Mon 5/5/25	Fri 5/23/25															
6		Structural Steel	40 days	Mon 5/19/25	Fri 7/11/25	5														
7		Demo/Masonry	5 days	Mon 6/30/25	Fri 7/4/25	6														
8		Framing/Sheathing/Barri	25 days	Mon 6/23/25	Fri 7/25/25	5														
9		Roofing	5 days	Mon 6/30/25	Fri 7/4/25	6														
10		Granite Panels/Sealant	25 days	Mon 7/28/25	Fri 8/29/25	9														
11		HVAC	100 days	Tue 4/1/25	Mon 8/18/25															
12		Set New Unit and Tie in	15 days	Mon 8/11/25	Fri 8/29/25	10														
13		Electrical	85 days	Tue 4/1/25	Mon 7/28/25															
14		Testing	5 days	Mon 9/8/25	Fri 9/12/25	12														
15		Punch List	5 days	Mon 9/15/25	Fri 9/19/25	14														
16		Clean Up/Demobilize	2 days	Mon 9/22/25	Tue 9/23/25	15														





Project: Cumberland County Co
Date: Thu 10/3/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			


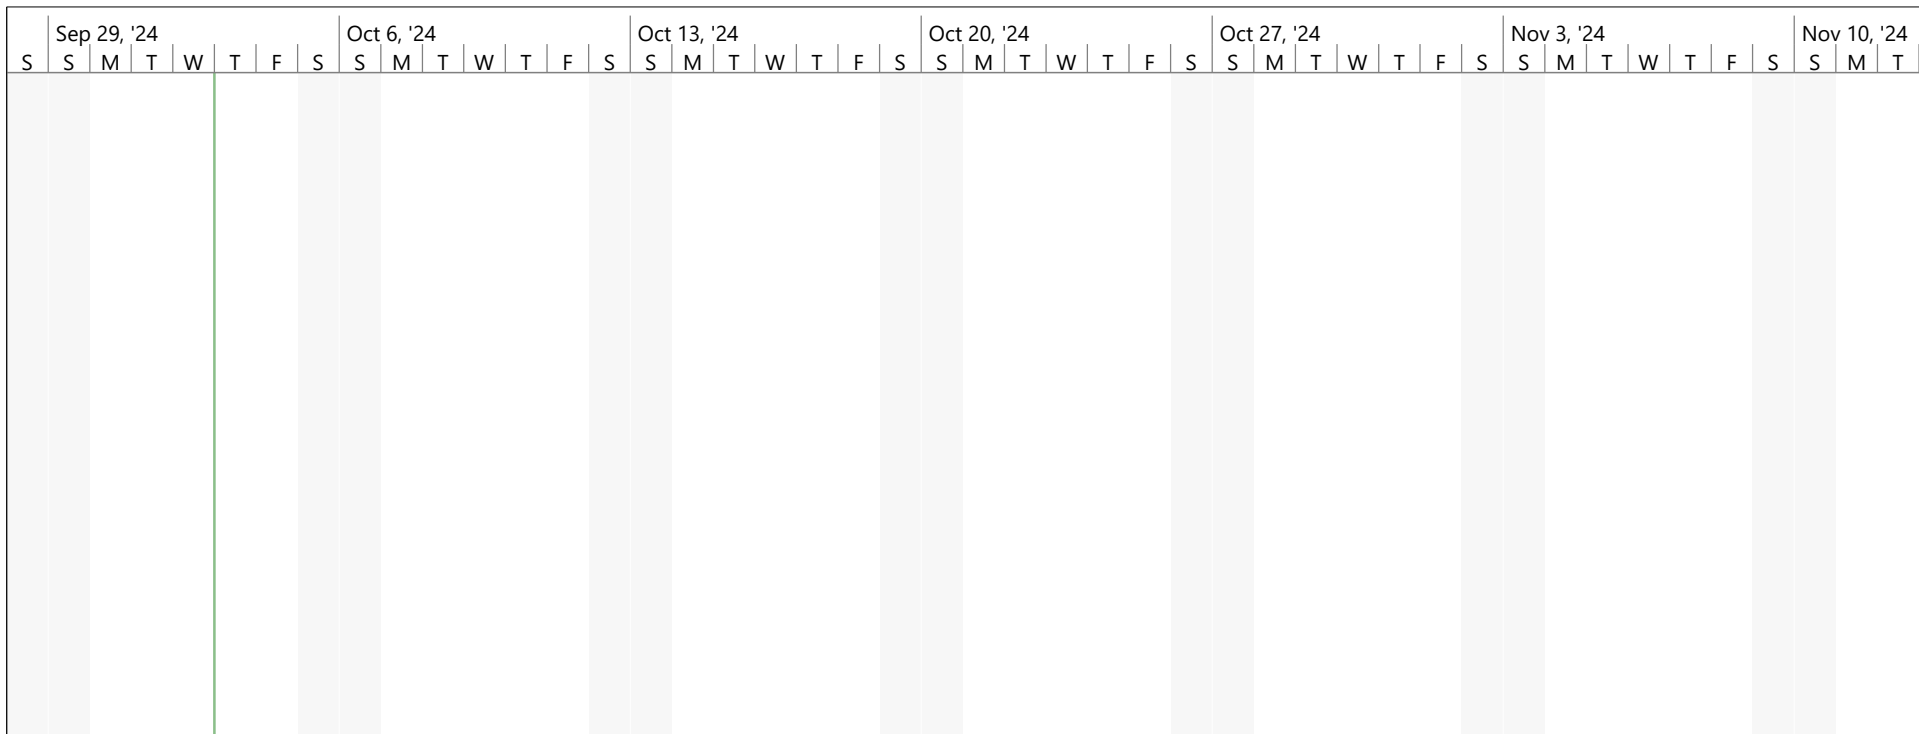


Project: Cumberland County Co
 Date: Thu 10/3/24



Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			




Project: Cumberland County Co Date: Thu 10/3/24	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			



Project: Cumberland County Co Date: Thu 10/3/24	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

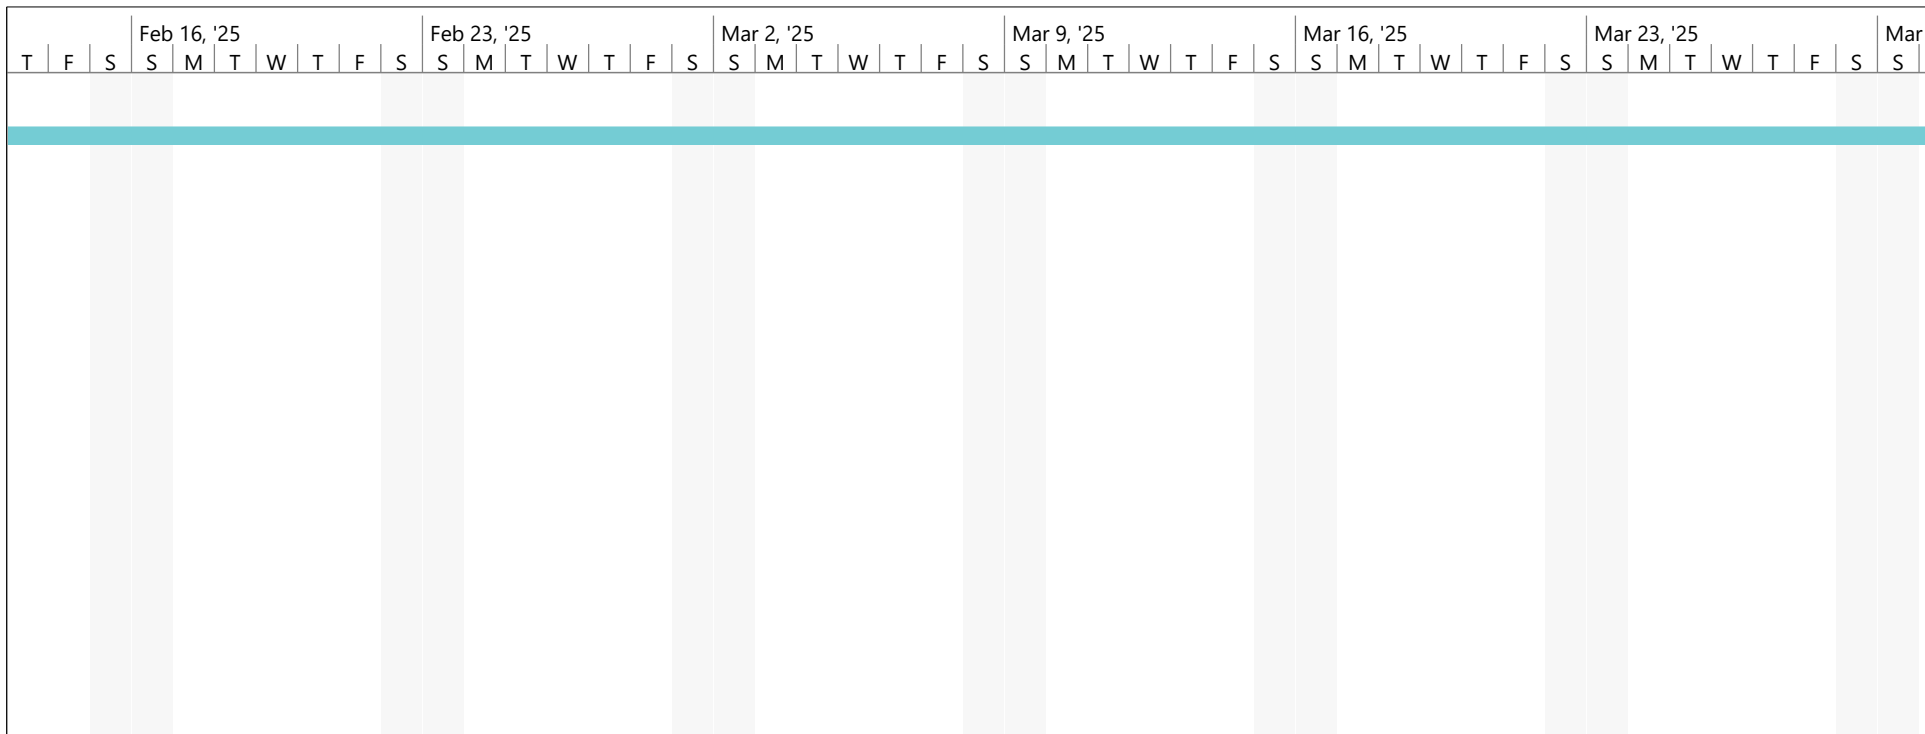


Project: Cumberland County Co Date: Thu 10/3/24	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

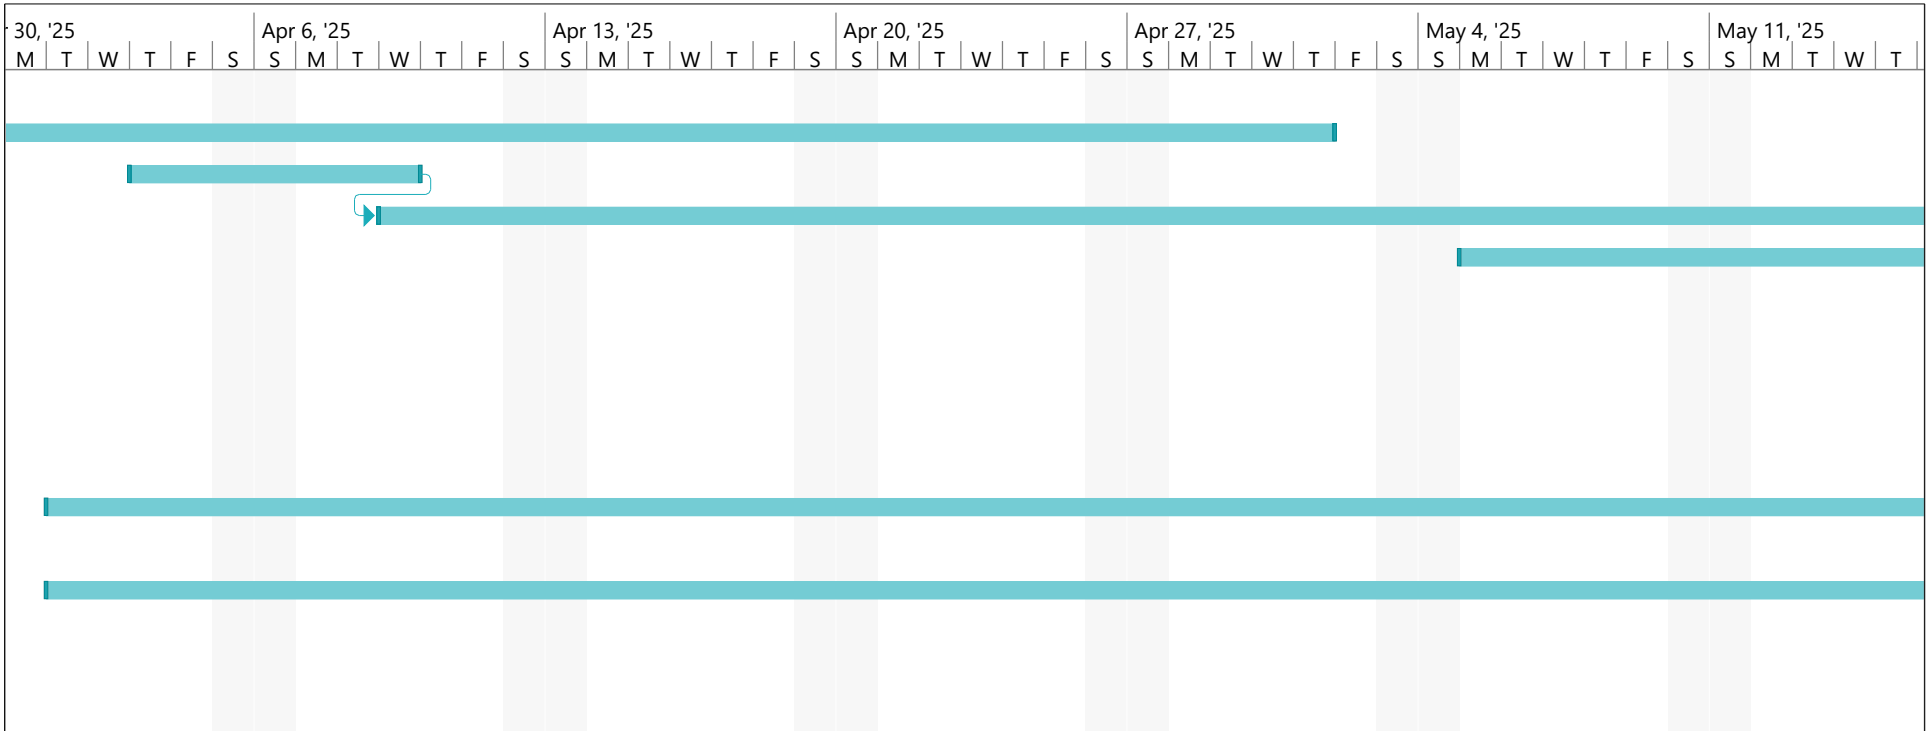


Project: Cumberland County Co
 Date: Thu 10/3/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

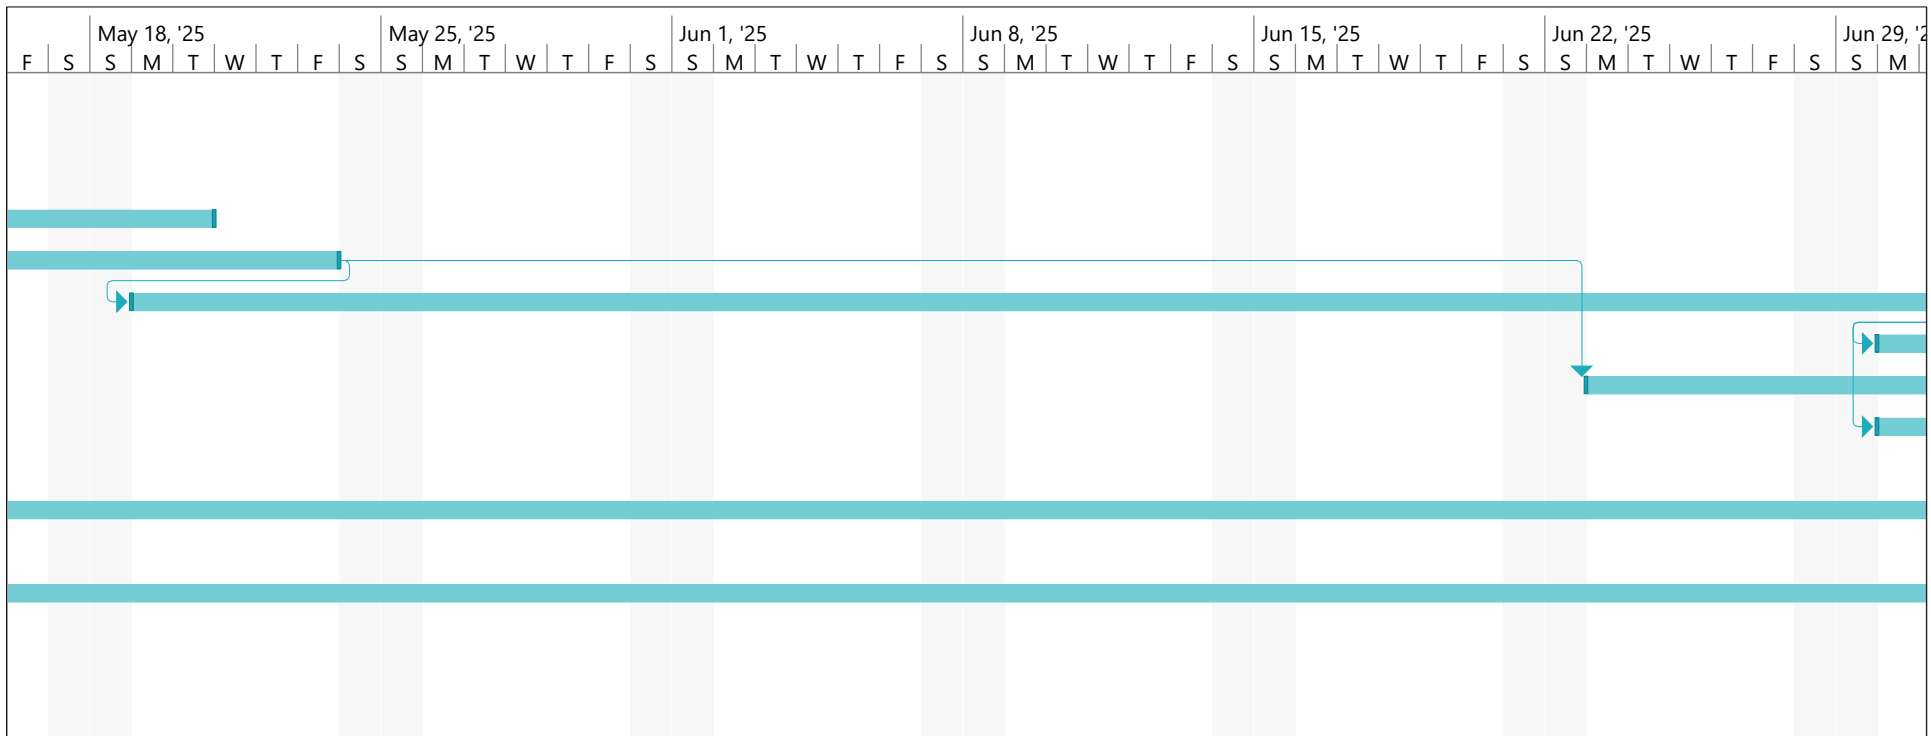


Project: Cumberland County Co
 Date: Thu 10/3/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

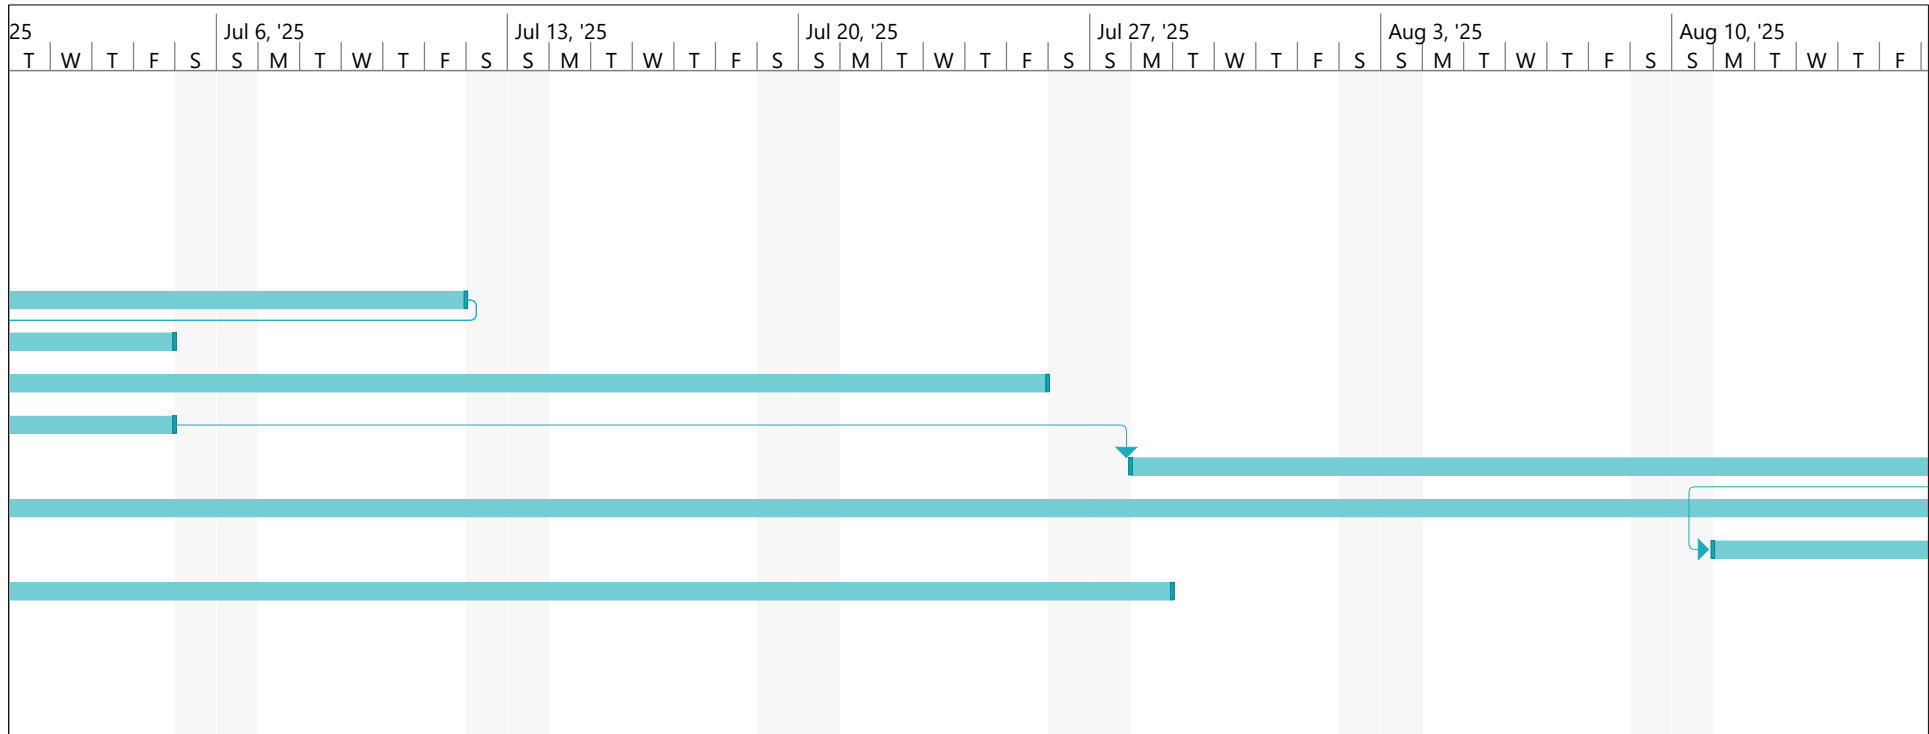

Project: Cumberland County Co
 Date: Thu 10/3/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

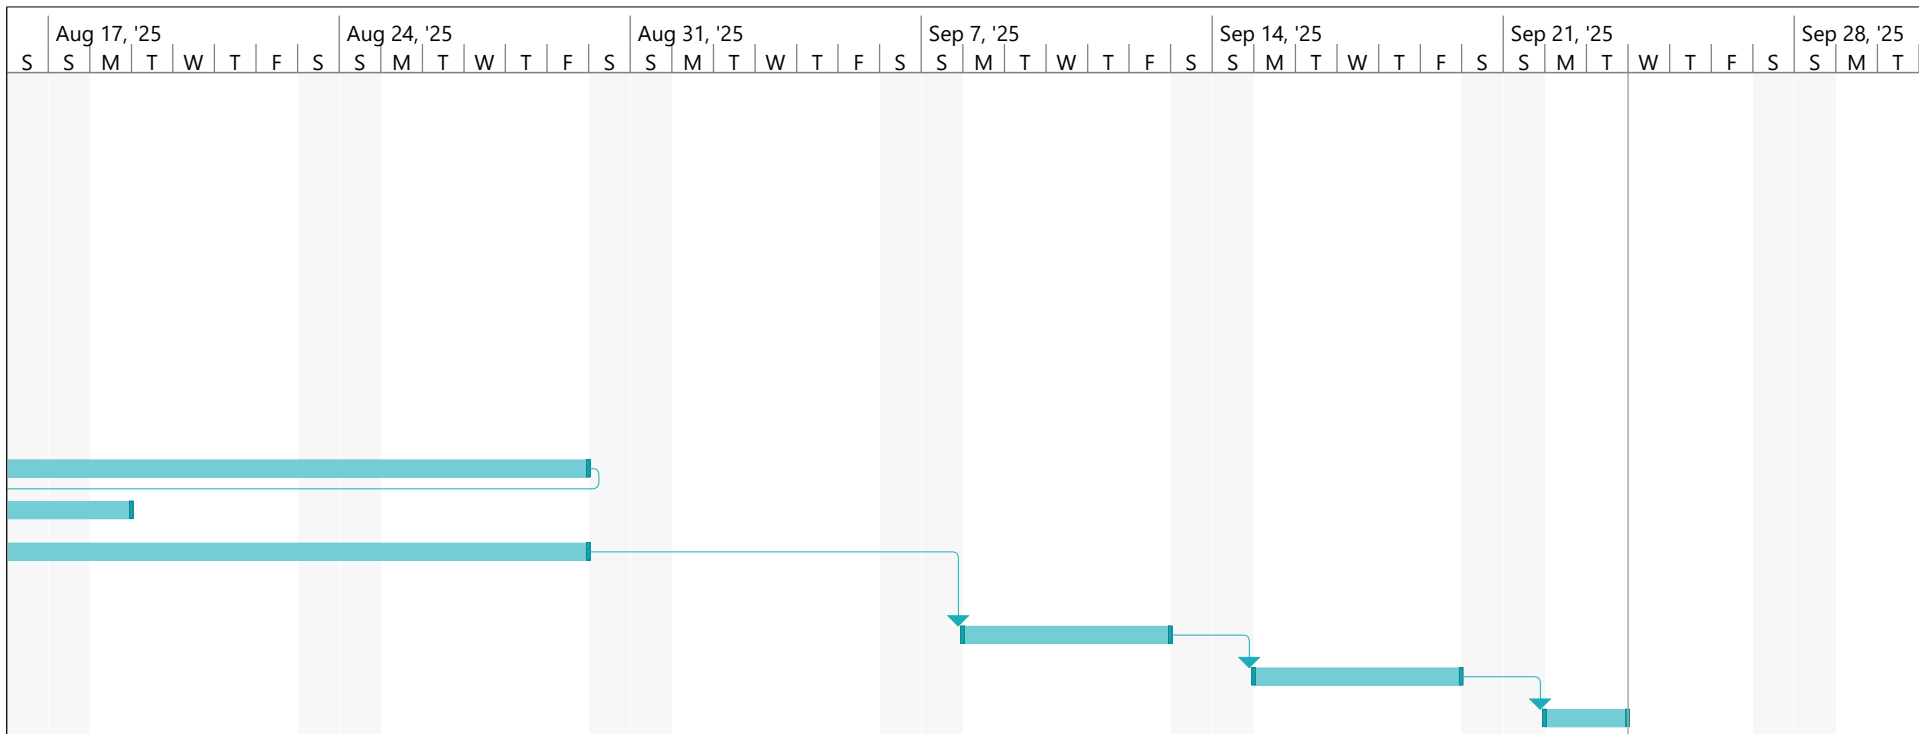

Project: Cumberland County Co
Date: Thu 10/3/24

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			
